| Contents | Reference to last Measurement |
|---|---|
| 7 | 8 |
| | |

**M. A. R. 57 (Rule 116)**
Measurement Book

**No. B**

501910

Serial No. Hand final Bill

Name of Work Construction of Culvert From ward No.11 Cross to Nagarampur sub-Div

Name of Contractor of nature of Agency M/s. K.R. Construction Jakkur Bore-64

Date of commencement of work D.O.L: 21-09-2020

| Date | Full description, etc, of work | Dimensions | | | | Contents | Reference to last Measurement |
|---|---|---|---|---|---|---|---|
| | | Number | Length | Breadth | Depth | | |
| 1 | 2 | 3 | 4 | 5 | 6 | 7 | 8 |
| | Est cost Rs: 20.00 lakhs<br>Job code No: 011-20-00016J5<br>Head of A/c: P1771<br>Work order No: BBMP/CE(TP)/WO/83/2020-21 Dt: 20/05/2020, | | | | | | |
| (1911) | Earth work excavation by manual means in ordinary soil in trenches an average horizontal up to 30m and an average lift up to 0.5m, excavated surface trimmed and sides nearly dressed etc.—<br>Quantity as per Pre-measurement Recorded vide P.No: 906 of this mm<br>= 189.60 cum<br>@ Rs: 207.05/cum = 26834.00/— | | | | | | |

# MEASUREMENT BOOK

| Date | Full description, etc, of work | Dimensions | | | | Contents | Reference to last Measurement |
|---|---|---|---|---|---|---|---|
| | | Number | Length | Breadth | Depth | | |
| 1 | 2 | 3 | 4 | 5 | 6 | 7 | 8 |
| item no 2) | Providing and laying plain cement concrete of mix 1:3:6 with OPC cement at ground, with crushed Hamm and down size graded granite metal coarse aggregate @ 0.84 cum and fine aggregate @ 0.56 cum, in foundation mechanically mixed, placed in foundation and compacted etc — | | | | | | |
| | Quantity as per Pre-measurement Recorded vide p.no: 907 of this MB = 16.00 cum | | | | | | |
| | @ Rs: 4603.19/cum = 74572.00/— | | | | | | |
| item no 5) | Providing and constructing granite/trap/basalt size stone masonry in basement with cement mortar 1:6 comp of stong chistic approved in course not less than 15cm high bond stones at two mtr apart etc — | | | | | | |
| | Quantity as per Pre-measurement Recorded vide p.no: 908 of this MB = 56.70 cum | | | | | | |
| | @ Rs 4934.37/cum 279779.00 | | | | | | |

Serial No. .....
Name of Work .....
Name of Contractor of nature
Date of commencement of wo

| Date | Full description, etc |
|---|---|
| 1 | 2 |
| (item 4) | Providing ruled p 1:3 grade slop, |
| | Quantity as per |
| (item 5) | providing pre-co |
| | Quantity as per |
| | @ Rs: 4934.37/cum |

**M. A. R. 57 (Rule 116)**
Measurement Book

**No. B**

501911

Serial No. .....

Name of Work ..... From..... To.....

Name of Contractor of nature of Agency .....

Date of commencement of work .....

| Date | Full description, etc, of work | Dimensions | | | | Contents | Reference to last Measurement |
|---|---|---|---|---|---|---|---|
| | | Number | Length | Breadth | Depth | | |
| 1 | 2 | 3 | 4 | 5 | 6 | 7 | 8 |
| | (Item 4) Providing ruled pointing 20mm deep to carried stone masonry with cement mortar 1:3 (one part cement three parts sand) 20mm deep, after raking joints to depth 20mm neatly using etc-- complete as per pre-measurement Deptt. vide page no: 908 of this MB = 108.00 Sqm @ Rs: 127.71/Sqm = 13801.00/- | | | | | | |
| | (Item 5) providing precast slab 40mm thick including cost of all materials etc-- | | | | | | |
| | Sewerage Garden 1st Cross EW | 15 | 1.50 | 0.60 | | 1170 | |
| | Sewerage Garden 1st Cross NW | 8 | 1.50 | 0.60 | | 720 | |
| | Sewerage Garden 2nd Cross EW | 14 | 1.50 | 0.60 | | 12.60 | |

# MEASUREMENT BOOK

| Date | Full description, etc, of work | Dimensions | | | | Contents | Reference to last Measurement |
|---|---|---|---|---|---|---|---|
| | | Number | Length | Breadth | Depth | | |
| 1 | 2 | 3 | 4 | 5 | 6 | 7 | 8 |
| | Singapura paradise 6th main | ~~13~~ | 1.50 | 0.60 | | 11.70 | |
| | Srinidhi Layout 8th D main Road | ~~13~~ | 1.50 | 0.60 | | 11.70 | |
| | sai Gardens main Road | ~~13~~ | 1.50 | 0.60 | | 11.70 | |
| | Sai Gardens 1ST CROSS E1S | ~~11~~ | 1.80 | 0.60 | | 11.88 | |
| | Sai Gardens 1st CROSS W1S | ~~11~~ | 1.80 | 0.60 | | 11.88 | |
| | | | | TOTAL QTY | = | 90.36 sqm | |
| | | | | Limited TO tender QTY | = | 90.00 Sqm | |
| | | | | @ Rs: 4599.88/sqm = | | 413969.00/- | |
| Item NO.6) | providing precast slabs of 10mm thick including cost of all materials etc-- | | | | | | |
| | missing covering slabs | | | | | | |

CFO
Verified
Engineer
Division

**M. A. R. 57 (Rule 116)**
Measurement Book

**No. B** 501912

Serial No. .....
Name of Work ..... From..... To.....
Name of Contractor of nature of Agency .....
Date of commencement of work .....

| Date | Full description, etc, of work | Dimensions | | | | Contents | Reference to last Measurement |
|---|---|---|---|---|---|---|---|
| | | Number | Length | Breadth | Depth | | |
| 1 | 2 | 3 | 4 | 5 | 6 | 7 | 8 |
| | Srinidhi Layout 4TH 'C' CROSS | 1 | 63.00 | 0.90 | = | 56.70 Sqm | |
| | Srinidhi Layout 8TH main | 1 | 46.00 | 0.90 | = | 41.40 | |
| | Sai Gowrav main Road D 1ST CROSS | 1 | 35.00 | 0.90 | = | 31.50 | |
| | Srinidhi Layout 8TH D main | 1 | 60.00 | 0.90 | = | 54.00 | |
| | Srinidhi Layout opp Girijamma Hall | 1 | 9.50 | 0.90 | = | 8.55 | |
| | Veerappa Gowrav main Road | 1 | 37.00 | 0.90 | | 33.30 | |
| | Srinidhi Layout 8TH E main | 1 | 42.00 | 0.90 | = | 42.30 | |
| | Singappa Paradise | 1 | 43.00 | 0.90 | = | 38.70 | |
| | | | | D.Total Qty | = | 306.45 Sqm | |

# MEASUREMENT BOOK

| Date | Full description, etc, of work | Dimensions | | | | Contents | Reference to last Measurement |
|---|---|---|---|---|---|---|---|
| | | Number | Length | Breadth | Depth | | |
| 1 | 2 | 3 | 4 | 5 | 6 | 7 | 8 |
| | Limited to Tender Quantity = 306.00 Sqm @ Rs. 1984.11/Sqm = 607188.00 | | | | | | |
| Item No 7) | Providing and laying in position Plain cement concrete 1:2:4 with cement @ 250 kgs/cum and down size graded granite metal coarse aggregate @ 0.8 cum and fine aggregate etc. | | | | | | |
| | Current coping: | | | | | | |
| | Senappa Garden 1st CROSS E/S | 1 | 7.60 | 1.50 | 0.10 | 1.14 | |
| | Senappa Garden 1st CROSS W/S | 1 | 4.85 | 1.50 | 0.10 | 0.73 | |
| | Senappa Garden 2nd CROSS E/S | 1 | 8.60 | 1.50 | 0.10 | 1.29 | |
| | Singapur paradise 6th main | 1 | 8.00 | 1.50 | 0.10 | 1.20 | |
| | Srinidhi layout 8th D main Road | 1 | 7.60 | 1.50 | 0.10 | 1.14 | |
| | Sai Garden main Road | 1 | 7.60 | 1.50 | 0.10 | 1.14 | |
| | Sai Garden 1st CROSS E/S | 1 | 6.80 | 1.50 | 0.10 | 1.02 | |
| | Sai Garden 1st CROSS W/S | 1 | 6.60 | 1.50 | 0.10 | 0.99 | |

Serial No. .....
Name of Work .....
Name of Contractor of nature of Age
Date of commencement of work .....

| Date | Full description, etc, of wo |
|---|---|
| 1 | 2 |
| | Ramp |
| | Senappa Garden 1st CROSS |
| | Senappa Garden 1st CROS |
| | Senappa Garden 2nd CR |
| | Singapur paradise 6th m |
| | Srinidhi layout 8th main |
| | Sai Garden main Road |
| | Sai Garden 1st CROSS C |
| | Sai Garden 1st CROSS W |

**M. A. R. 57 (Rule 116)**
Measurement Book

**No. B** 501913

Serial No. .....
Name of Work ..... From..... To.....
Name of Contractor of nature of Agency .....
Date of commencement of work .....

| Date | Full description, etc, of work | Dimensions: Number | Length | Breadth | Depth | Contents | Reference to last Measurement |
|---|---|---|---|---|---|---|---|
| 1 | 2 | 3 | 4 | 5 | 6 | 7 | 8 |
| | Ramp | | | | | | |
| | Senappa Garden 1st cross E/S | 2 | 7.70 | 1.00 | 0.10 | 1.54 | |
| | Senappa Garden 1st cross W/S | 2 | 4.85 | 1.00 | 0.10 | 0.97 | |
| | Senappa Garden 2nd cross E/S | 2 | 8.60 | 1.20 | 0.10 | 2.06 | |
| | Singapur paradise 6th main | 2 | 8.00 | 1.00 | 0.10 | 1.60 | |
| | Srinidhi layout 8th main | 2 | 7.60 | 1.00 | 0.10 | 1.52 | |
| | Sai Garden main Road | 2 | 7.60 | 1.00 | 0.10 | 1.52 | |
| | Sai Garden 1st cross E/S | 2 | 6.80 | 1.00 | 0.10 | 1.36 | |
| | Sai Garden 1st cross W/S | 2 | 6.60 | 1.00 | 0.10 | 1.32 | |
| | | | | Total Quantity = | | 20.52 | |
| | | | | Say = | | 21.00 cum | |
| | | | | @ Rs. 47534.38/cum | | | 998482.00 |

cafe market

# MEASUREMENT BOOK

| Date | Full description, etc, of work | Dimensions | | | | Contents | Reference to last Measurement |
|---|---|---|---|---|---|---|---|
| | | Number | Length | Breadth | Depth | | |
| 1 | 2 | 3 | 4 | 5 | 6 | 7 | 8 |
| | | | | Total Amount | | = | 15,15,955.00 |
| | | | | GST @ 6% | | = | 1,81,915.00 |
| | | | | Grand Total | | = | 16,97,870.00 |
| | | | | 21-09-2020 | | | |

Certificate:

1) Certified that the above work done satisfactory

2) Certified that the contractor has clear all the debris from the work spot

3) No materials issued from Departmentally.

21-09-2020

Assistant Executive Engineer
Vidyaranyapura Sub Division
BBMP, Bangalore - 97

Assistant Executive Engineer
Vidyaranyapura Sub Division
BBMP, Bangalore - 97

21/9/20

| Contents | Reference to last Measurement |
|---|---|
| 7 | 8 |
| | 15,15,955.00 |
| | 1,81,915.00 |
| | 16,97,870.00 |

Executive Engineer
Singapura Sub Division
P.B. Bangalore-97

21/9/20

**M. A. R. 57 (Rule 116)**
Measurement Book

**No. B**

501914

Serial No. .....
Name of Work ..... From..... To.....
Name of Contractor of nature of Agency .....
Date of commencement of work .....

| Date | Full description, etc, of work | Dimensions: Number | Length | Breadth | Depth | Contents | Reference to last Measurement |
|---|---|---|---|---|---|---|---|
| 1 | 2 | 3 | 4 | 5 | 6 | 7 | 8 |
| | 4.25×1.50 | | | | | | |
| | 7.60×1.50m | | | | | | |
| | 1st cross | | | | | | |
| | Seenappa Garden | | | | | | |
| | 8.60×1.50 | | | | | | |
| | 2nd cross | | | | | | |
| | INDEX: | | | | | | |
| | - culvert | | | | | | |
| | | | | | SWD | | |
| | | | | | 6th main | | Singapura paradise |
| | | | | | 8.00×1.50m | | |
| | | | | | | Main Road | |

# MEASUREMENT BOOK

| Date | Full description, etc, of work | Dimensions | | | | Contents | Reference to last Measurement |
|---|---|---|---|---|---|---|---|
| | | Number | Length | Breadth | Depth | | |
| 1 | 2 | 3 | 4 | 5 | 6 | 7 | 8 |

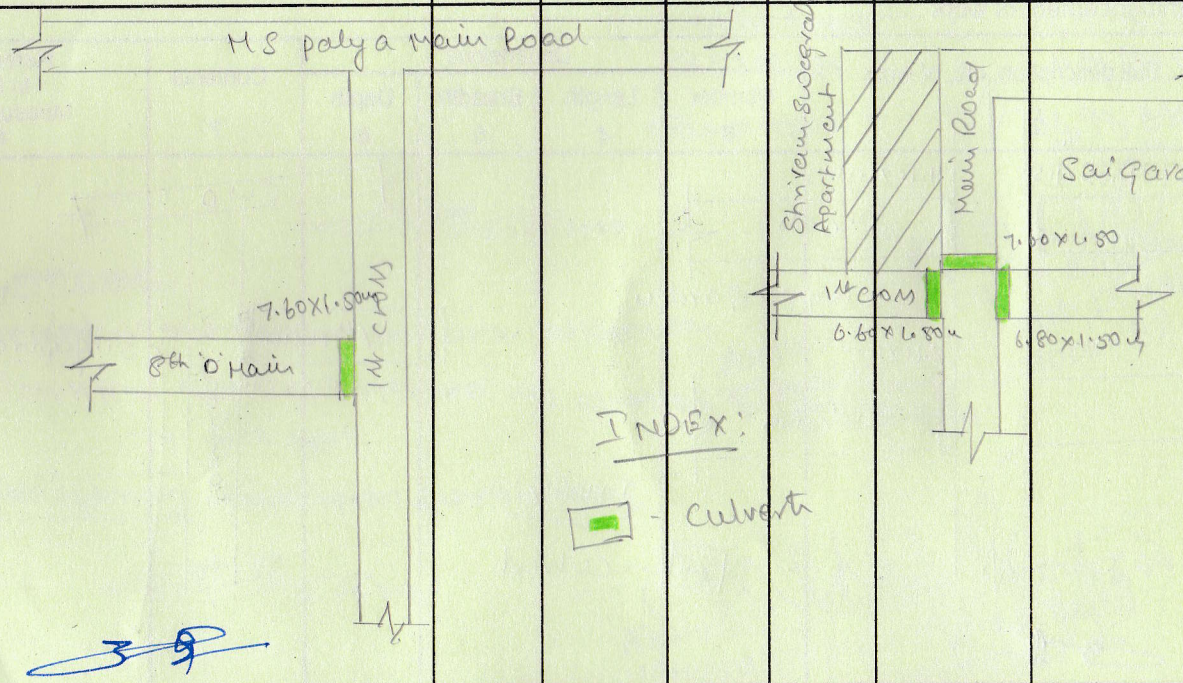


Serial No. .....
Name of Work .....
Name of Contractor of nature of A
Date of commencement of work ..

| Date | Full description, etc, of |
|---|---|
| 1 | 2 |
